


# OSG 243

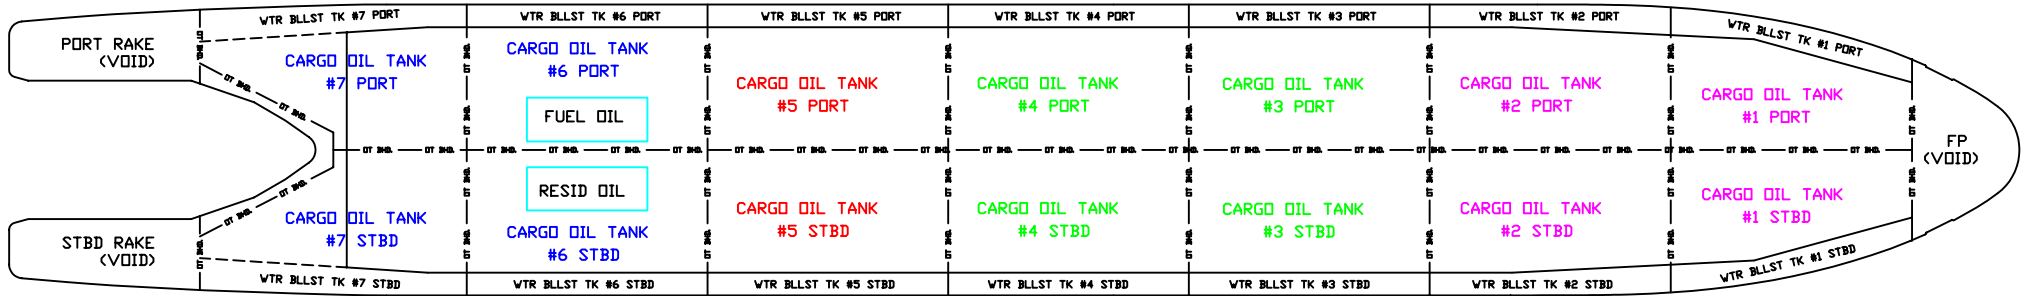

## ARRANGEMENT

### NATURAL SEGREGATIONS

TANK NAME	PUMP #
#1Ving P.	1
#1Ving S.	1
#2 Wing P.	1
#2 Wing S.	1
#3 Wing P.	2
#3 Wing S.	2
#4 Wing P.	2
#4 Wing S.	2
#5 Wing P.	3
#5 Wing S.	3
#6 Wing P.	4
#6 Wing S.	4
#7 Wing P.	4
#7 Wing S.	4

### CARGO OIL TANKS

TANK NAME	LOCATION	100% FULL CU. METER	100% FULL BARRELS	98% FULL CU. METER	98% FULL BARRELS
COT 1P	10-19	2328.10	14,652.20	2281.57	14,359.16
COT 1S	10-19	2328.10	14,652.20	2281.57	14,359.16
COT 2P	19-28	2988.20	18,806.38	2928.44	18,430.25
COT 2S	19-28	2988.20	18,806.38	2928.44	18,430.25
COT 3P	28-30F	3045.50	19,166.93	2984.57	18,783.59
COT 3S	28-30F	3045.50	19,166.93	2984.57	18,783.59
COT 4P	30F-36	3045.50	19,166.93	2984.57	18,783.59
COT 4S	30F-36	3045.50	19,166.93	2984.57	18,783.59
COT 5P	36-44	3045.50	19,166.93	2984.57	18,783.59
COT 5S	36-44	3045.50	19,166.93	2984.57	18,783.59
COT 6P	44-52	3020.45	19,009.32	2960.03	18,629.13
COT 6S	44-52	3020.45	19,009.32	2960.03	18,629.13
COT 7P	52-62	1759.15	11,071.30	1720.40	10,849.87
COT 7S	52-62	1759.15	11,071.30	1720.40	10,849.87
TOTAL		38 464.80	242,079.98	37 688.30	237,238.36

### DEADWEIGHT

ITEM		DEADWEIGHT		DISPLACEMENT (LONG TONS)
		FREEBOARD	KEEL DRAFT	
TROPICAL FRESH WATER	TF	4'-6 7/8"	32'-11 15/16"	30,851
FRESH WATER	F	5'-3 3/4"	32'-3 1/16"	29,969
TROPICAL	T	5'-4 11/16"	32'-2 1/8"	30,769
SUMMER	S	6'-0 9/16"	31'-6 1/4"	29,967
WINTER	W	6'-8 7/16"	30'-10 3/8"	29,167
